



**Appendix F - A34 SPRINT Programme  
(January 2021)**

**Package A Schedule**



Activity ID	Activity Name	Responsible Manager	Original Duration	Remaining Duration	Start	Finish	2021												2022																																																																																			
							Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov																																																																						
<b>A34 &amp; A45 DRAFT Rv17</b>							291																								291																								01-Dec-20																								08-Feb-22																							
<b>Target Cost and Contract</b>							111																								111																								01-Dec-20																								21-May-21																							
<b>Plan B</b>							111																								111																								01-Dec-20																								21-May-21																							
A34							111																								111																								01-Dec-20																								21-May-21																							
<b>A34</b>							111																								111																								01-Dec-20																								21-May-21																							
<b>Package A (Section 1 &amp; 2)</b>							111																								111																								01-Dec-20																								21-May-21																							
A3740	Develop Tender Packs(Including Quality, Price Questions,Evaluation Criteria & Contract Data Part 1)	SW & CP	7	7	01-Dec-20*	09-Dec-20																																																																																																
A3750	Collate Detailed Tender Pack(Drawings,Spec & BoQs)	AECOM & MD	7	7	01-Dec-20	09-Dec-20																																																																																																
A4940	Package A		111	111	01-Dec-20	21-May-21																																																																																																
A4300	Governance Process - Produce Procurement Strategy & Price Quality Report for Authorisation by Senior Management	SW	5	5	03-Dec-20	09-Dec-20																																																																																																
A4270	OJEU Compliance Review Undertaking by F&G	F&G	5	5	10-Dec-20	16-Dec-20																																																																																																
A3760	F&G Collate Tender Information & Finalise Tender Packs	F&G	10	10	17-Dec-20	13-Jan-21																																																																																																
A3770	Tender Issue via Bravo Solutions - Pkg 1 & 2	SW	0	0		16-Feb-21*																																																																																																
A3780	Clarification Period (including cut-off)		15	15	17-Feb-21	09-Mar-21																																																																																																
A3790	Tender Period		25	25	17-Feb-21	23-Mar-21																																																																																																
A3800	Closing Date for Clarification		0	0		09-Mar-21																																																																																																
A4280	Agree Budget Estimates	OJ	1	1	22-Mar-21	22-Mar-21																																																																																																
A3810	Tender Return		0	0		23-Mar-21																																																																																																
A3820	Evaluate Tenders & Identify Supplier	F&G & Team	14	14	24-Mar-21	13-Apr-21																																																																																																
A3850	Preparation of Draft Contract ready for Contract Award	Legal	5	5	24-Mar-21	30-Mar-21																																																																																																
A4290	Governance Process - Produce Contract award Report for Authorisation by Senior Management	SW	10	10	31-Mar-21	14-Apr-21																																																																																																
A3830	Contract Discussions & Finalise Contract		5	5	07-Apr-21	13-Apr-21																																																																																																
A3840	Sprint Programme Board to Approve Contract Award		1	1	14-Apr-21	14-Apr-21																																																																																																
A3870	Contract Signature		5	5	15-Apr-21	21-Apr-21																																																																																																
A3860	Mobilisation Meeting		1	1	15-Apr-21	15-Apr-21																																																																																																
A3880	Contract Award		0	0		21-Apr-21																																																																																																
A3890	Mobilisation		20	20	22-Apr-21	20-May-21																																																																																																
A3900	Commence Construction		0	0	21-May-21																																																																																																	
<b>Construction</b>							180																								180																								21-May-21																								08-Feb-22																							
<b>A34 Construction</b>							180																								180																								21-May-21																								08-Feb-22																							
A4250	Section 2 Complete (Including Snagging)		0	0		12-Jan-22																																																																																																
A4260	Section 1 Complete (Including Snagging)		0	0		08-Feb-22																																																																																																
<b>Pre-Commonwealth</b>							180																								180																								21-May-21																								08-Feb-22																							
A1430	Section 2 - Scott Arms A4041 to Aston University Recreation Centre CH4370 to 6300		161	161	21-May-21	12-Jan-22																																																																																																
A1060	Section 1- Broadway A4148 to Walsall TC CH0 to 2400		180	180	21-May-21	08-Feb-22																																																																																																

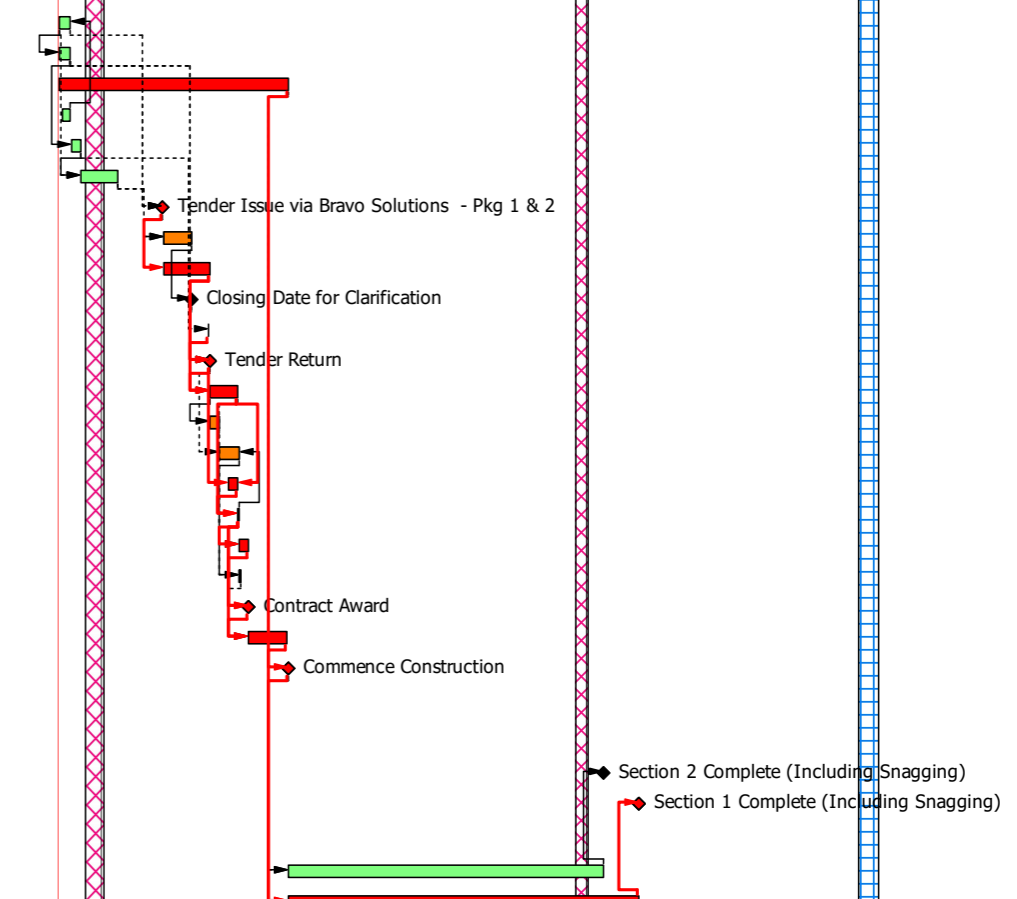

█ Actual Work      █ Remaining Work      █ Critical Remaining Work  
█ Near CP      ◆ Milestone      ◆ Critical Milestone

Page 1 of 1  
 Revision:SPR.Rv17  
 Checked: admin      Approved by:  
 Every minute spent in planning saves 10mins in execution

Printed: 04-Jan-21 14:00  
 DataDate: 30-Nov-20  
 TFWM\_Sprint\_Full Schedule(Package A)
